CITY OF LITTLE ROCK Public Works Department

Ward 4

2016 to 2018 Street and Drainage Program Meeting



Ward 4

Sales Tax/Bond Projected Allocation

	 2013-2015	2016-2018	2019-2		2019-2021	
Sales Tax	\$ 2,600,000	\$ 2,600,000	*	\$	2,600,000	*
Bond	\$ 6,700,000			\$	5,750,000	*
Total	\$ 9,300,000	\$ 2,600,000	*	\$	8,350,000	*

April 1, 2015

* Projected Funding






Ward 4 - 2013 to 2015 Bond/Sales Tax Summary

- A total of \$2,600,000 in Sales Tax funding was allocated.
- A total of \$6,700,000 in Bond Issues was allocated.
- In the 2013 to 2015 project request list, there were 30 jobs requested.
- A total of 6 Bond Program jobs and 11 Sales Tax Program jobs were selected and are in the process of design, bidding, and construction.
- Currently 13 jobs (76%) are in design, 2 jobs (12%) are currently in construction, and 2 jobs (12%) are totally complete.



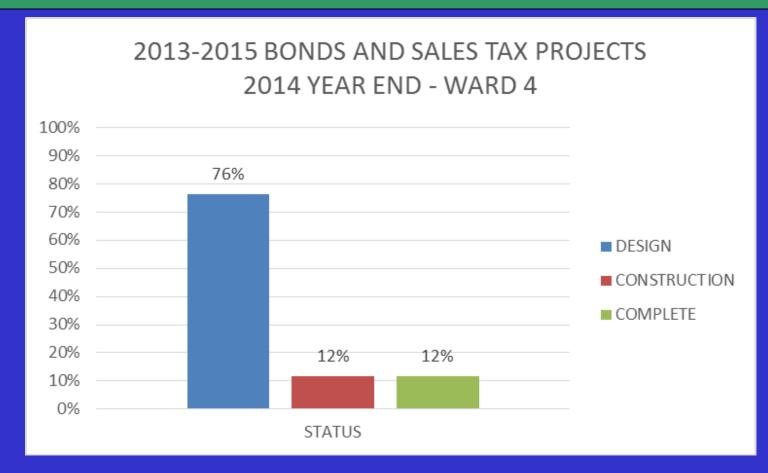

April 1, 2015 4



Ward 4 Sales Tax Project Status

Request #	Location	Description	Status	Anticipated Bid Quarter
4-6	Rodney Parham	Add dedicated bike lanes from Valley Club north to Rocky Valley (560 lf). Add sharrows bike path from Rocky Valley to Cantrell. (2300 lf)	In Construction	
4-7e	Pleasant Valley	Improve drainage at St. James/Fulbright School.	In Design – 60% complete	2 nd - 2015
4-10	Pleasant Valley	Install Roundabout at Pleasant Valley and Arkansas Valley.	Project Canceled	
4-100	White Willow Ct	Install underground drainage.	In Design – 90% complete	2 nd - 2015
4-101	River Mtn Rd	Corrugated metal pipe rehabilitation. Estimate is to pave invert.	Project Complete	
4-102	Gristmill Rd	Install underground drainage.	In Design – 90% complete	2 nd - 2015
4-103	Longlea Ct	Install inlets and pipe upstream from #63 Longlea Ct.	In Design – 60% complete	3 rd - 2015
4-104	Echo Valley Ct	Enclose ditch beside #9905 Echo Valley Ct.	In Design – 60% complete	3 rd - 2015
4-105	Rodney Parham at Buff Lane	Improve underground drainage system at Buff Lane.	In Design – 60% complete	2 nd - 2015
4-106	Russ St	Improve drainage along Russ St.	In Design – 30% complete	4 th - 2015
4-107	Northbrook Circle	Enclose open ditch from Northbrook Circle to Brookhaven Dr.	In Design – 90% complete	2 nd - 2015
4-108	Breckenridge Drive	Improve underground drainage system at 2601 Breckenridge Dr.	In Design – 90% complete	2 nd - 2015
		Misc. Sidewalk (Westbury Dr, Westchase Dr, Pleasant Valley, Arkansas Valley, Hidden Valley, Wentwood Valley)	Design Pending	

April 1, 2015 5



Ward 4 Bond Project Status

Request #	Location	Description	Status	Anticipated Bid Quarter
B-4a	Pinnacle Valley	Widen and improve to 2 lanes with bike lanes.	In Design - 90% complete	2 nd - 2015
B-4b	Ellis / Steven Drainage	Replace deteriorated corrugated metal pipe crossings on Ellis and Steven Drive.	In Design – 90% complete	2 nd - 2015
B-4c	El Dorado / Hinson Drainage	Replace three deteriorated corrugated metal pipe crossings under Hinson Rd.	Project Complete	
B-4d		Drainage improvements to open ditch from the north end of Secluded Hills Ct. to Cecil Drive.	In Construction	
B-4e	Hinson / Pebble Beach Intersection	Intersection improvements.	In Design 20% Complete	3 rd - 2015
B-4f	Rodney Parham / 430 Interchange	Grant match for interchange improvement project.	TBD	AHTD Controlled
Overlay	Program		In Construction – 45% Complete	

April 1, 2015



Ward 4 - 2016 to 2018 Project Request Summary

- Anticipated total of \$2,600,000 in Sales Tax funding will be allocated.
- Currently there are 6 new job requests.
- Deadline for Submission is May 1, 2015.
- For access to the Project Infrastructure Request form, citizens may:
 - 1. Pick up a copy here
 - 2. Go to website at http://www.littlerock.org/citydepartments/publicworks.aspx

 Halfway down the page under "Civil Engineering", click on "Infrastructure

 Request Form (Fillable)" link.
 - 3. Send form to: City of Little Rock Department of Public Works

Infrastructure Project Requests

701 West Markham

Little Rock, AR 72201

Email: PublicWorks@littlerock.org
