CITY OF LITTLE ROCK Public Works Department

Ward 5

2016 to 2018 Street and Drainage Program Meeting



Ward 5

Sales Tax/Bond Projected Allocation

	2013-2015		2016-2018			2019-2021		
Sales Tax	\$	2,600,000	\$	2,600,000	*	\$	2,600,000	*
Bond	\$	8,300,000				\$	5,750,000	*
Total	\$	10,900,000	\$	2,600,000	*	\$	8,350,000	*

April 9, 2015


* Projected Funding



Ward 5 - 2013 to 2015 Bond/Sales Tax Summary

- A total of \$2,600,000 in Sales Tax funding was allocated.
- A total of \$8,300,000 in Bond Issues was allocated.
- In the 2013 to 2015 project request list, there were 27 jobs requested.
- A total of 6 Bond Program jobs and 9 Sales Tax Program jobs were selected and are in the process of design, bidding, and construction.
- Currently 10 jobs (67%) are in design, 3 jobs (20%) are currently in construction, and 2 jobs (13%) are totally complete.



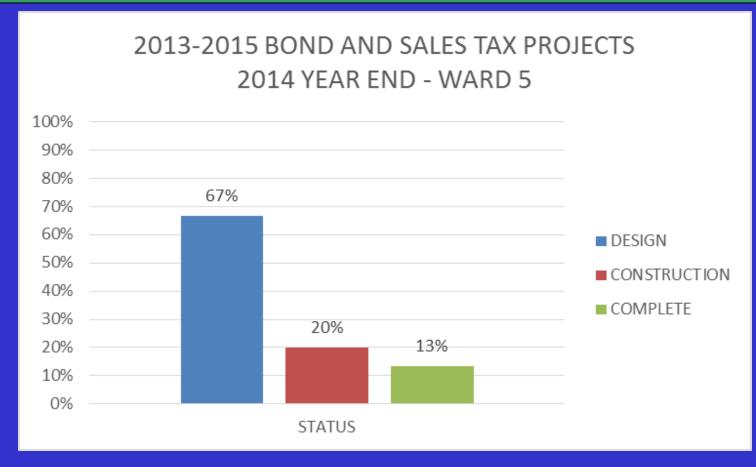

April 9, 2015 4



Ward 5 Sales Tax Project Status

Request #	Location	Description	Status	Anticipated Bid Quarter
5-5	Dorado Beach Dr	Install a larger pipe crossing at ditch on Dorado Beach Dr at approximately #1605	In Construction	
5-5a	Dorado Beach Dr	Enclose open ditch at 1411 Dorado Beach Dr.	In Construction	
5-14	Taylor Loop	Install segmental retaining wall in channel at the northeast corner of the intersection of Taylor Loop and Gooch Dr.	In Design – 60% complete	2 nd - 2015
5-16	Gamble Rd	Widen Gamble from Arthur north to mid 200 block .	In Design – 60% complete	2 nd - 2015
5-17	Heatherbrae/Glenn Valley	Install underground drainage system at the intersection of Heatherbrae and Glenn Valley.	In Design – 10% complete	2 nd - 2015
<i>5</i> -18c	Maywood Subdivision	Clean/repair drainage facilities from West & South Aberdeen drainage.	In Design – 60% complete	2 nd - 2015
5-24	LaMarche Drive	Construct new roadway for connection of LaMarche Dr north to Taylor Loop Rd	In Construction	
5-100	Bradberry Dr	Replace Pipes from 19 Bradberry to 2000 Sawgrass	Design Pending	4 th - 2015
5-101	Ledgelawn Dr	Replace undersized pipe at #7 Ledgelawn Dr.	Design Pending	4 th - 2015
		Misc. Traffic Calming	Design Pending	

April 9, 2015 5



Ward 5 Bond Project Status

Request #	Location	Description	Status	Anticipated Bid Quarter
B-5a	Pinnacle Valley	Widen and improve to 2 lanes with bike lanes.	In Design – 80% complete	2nd - 2015
B-5b	El Dorado / Hinson Drainage	Replace three deteriorated corrugated metal pipe crossings under Hinson Rd.	Project Complete	
B-5c	Hinson / Pebble Beach Intersection	Intersection improvements	In Design – 20% complete	3 rd - 2015
B-5d	Kanis Road	Design Kanis from Bowman to Gamble. Widen to three lane section with turn lanes at major intersections including curb, gutter, underground drainage system, sidewalks.	In Design – 50% complete	1 st - 2016
B-5e	Taylor Loop Road	Widen to collector standard including curb, gutter, underground drainage system, sidewalks.	In Design – 45% complete	2 nd - 2015
B-5f	Ranch Blvd Signal	Add signalized intersection.	Project Complete	
Overlay	Program		In Construction – 30% complete	

April 9, 2015



Ward 5 - 2016 to 2018 Project Request Summary

- Anticipated total of \$2,600,000 in Sales Tax funding will be allocated.
- Currently there are 14 new requests.
- Deadline for Submission is May 1, 2015.
- For access to the Project Infrastructure Request form, citizens may:
 - 1. Pick up a copy here
 - 2. Go to website at http://www.littlerock.org/citydepartments/publicworks.aspx

 Halfway down the page under "Civil Engineering", click on "Infrastructure

 Request Form (Fillable)" link.
 - 3. Send form to: City of Little Rock Department of Public Works

Infrastructure Project Requests

701 West Markham

Little Rock, AR 72201

Email: PublicWorks@littlerock.org
